

TEST CERTIFICATE



Name:Screw Spike(class 5.6)

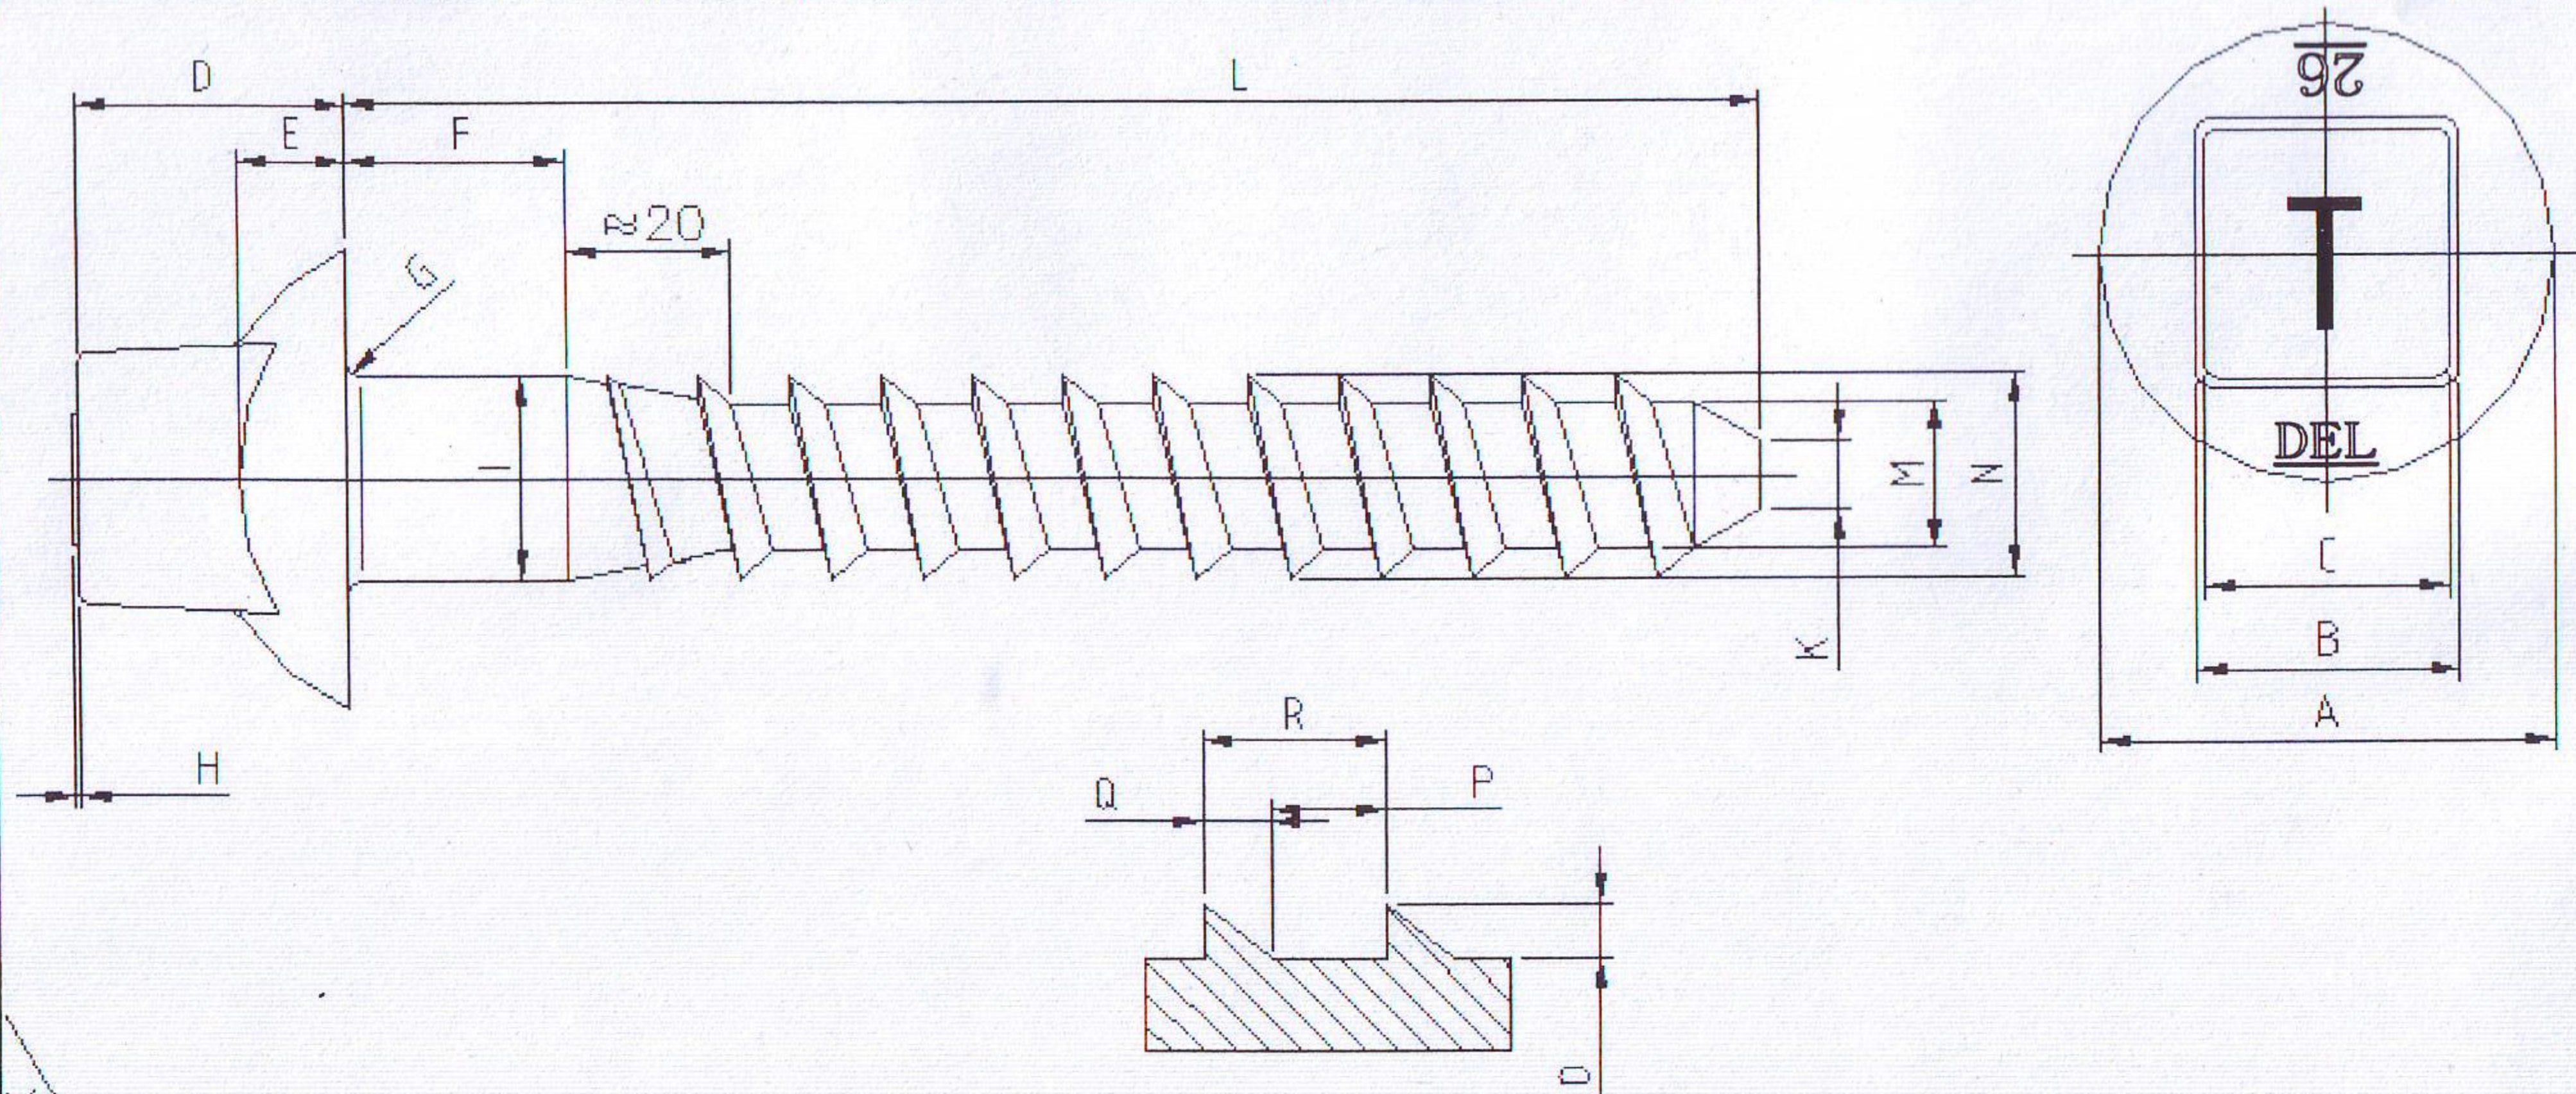
Contract No: 9523

Material: 55K

Specification: $\phi 22 \times 150$

Quantity:10000(Pieces)

Inspection date:2026.01.23

Raw material heat No.	Chemical Composition					Mechanical Properties			Dimension																	Coating (hot dipgalvanise) ≥55 μm	Result
	C%	Si%	Mn%	P%	S%	Tensile Strength N/mm²	Yield Point N/mm²	Elongation %	A	B	C	D	E	F	G	H	I	K	L	M	N	O	P	Q	R		
	0.32~0.38	0.10~0.35	0.60~0.90	≤0.030	≤0.035	≥500	≥300	≥20	∅49~51	□28.5~29.5	□26.5~27.5	28.5~31.5	11.2~12.8	21.5~26.5	R1.5	0.25~1.25	∅21.75~22.25	∅7.5~9	147~153	∅15.75~16.25	∅21.75~22.25	2.75~3.25	5.8~6.8	3.2~4.2	9.5~10.5		
G5310037 86	0.37	0.13	0.71	0.018	0.003	590	371	24	50	29.1	27.2	30.4	12.1	24.3	R1.5	0.65	22.1	8.6	152.1	16.1	22.1	3.1	6.3	3.7	10.1	73	Pass
	0.37	0.13	0.71	0.018	0.003	613	392	23	50.1	28.9	27.3	30.3	11.8	25.1	R1.5	0.72	22.0	8.3	150.8	16.0	22.0	3.0	6.3	3.7	9.9	87	Pass
	0.37	0.13	0.71	0.018	0.003	629	397	22	50.1	28.9	27.1	30.4	11.9	25.7	R1.5	0.83	22.0	7.8	151.6	16.1	22.1	3.1	6.3	3.7	9.9	94	Pass
	0.37	0.13	0.71	0.018	0.003	605	379	23	50.2	29.1	27.2	30.2	12.0	24.6	R1.5	0.74	21.9	8.2	152.4	15.9	21.9	3.0	6.2	3.8	10.1	69	Pass
	0.37	0.13	0.71	0.018	0.003	617	386	22	50.1	28.8	27.0	30.5	11.8	25.9	R1.5	0.79	21.9	8.9	150.2	16.0	22.0	3.0	6.2	3.7	10.0	76	Pass
																											

We hereby certify, that the material described above has been tested and complies with the terms of the order contract.

Inspector:Zhang-QuanHui

Checking:Yang-LiCheng

